

TS 30.1 | **If the Timing is Right**

Ann K. Myles

Land administration experience from Sweden, Zambia, Mozambique, Russia, Slovenia, Egypt, Belize, Lesotho etc.

ann-katrin.myles@lm.se

1 | LANTMÄTERIET

TS 30.1 | **If the Timing is Right**

Land Administration Project Components

- Legal and Land Policy
- Technical
- Institutional

2 | LANTMÄTERIET

TS 30.1 | **If the Timing is Right**

The Swedish Land Data Reform took 29 years

3 | LANTMÄTERIET

TS 30.1 | **If the Timing is Right**

More money than time – Very ambitious project designs !

4 | LANTMÄTERIET

TS 30.1 | **If the Timing is Right**

Example of Project Tenders:

- 8 months** • Develop Land Information Software and train technical staff and end users
- 3 years** • Develop a LA system that is fair, cost effective, decentralized and enhances tenure security
- 6 years** • Systematic Rural Land Titling and Cadastre Development, incl. systematic subdivision of land and the issue of 4 million land deeds and preparation of base maps

5 | LANTMÄTERIET

TS 30.1 | **If the Timing is Right**


A General Template for Computerization

6 | LANTMÄTERIET

TS 30.1

If the Timing is Right

The all-inclusive LA program

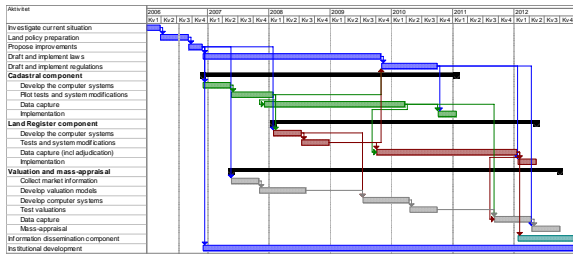

7

LANTMÄTERIET

TS 30.1

If the Timing is Right

Common timing problems:

- Premature data capture
- Computer equipment procured too early
- System is ready but is not legal


8

LANTMÄTERIET

TS 30.1

If the Timing is Right

.. for creating a digital cadastral database?

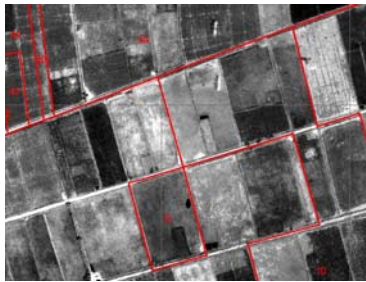

9

LANTMÄTERIET

TS 30.1

If the Timing is Right

If the timing is right....

...Land Administration project have a better chance to succeed!

10

LANTMÄTERIET
